

**YCC 2018 – MINIMUM PARK / MEMORIAL ROSE GARDEN / RIO ANIMAS PARK**

**MINIMUM PARK:** Will involve the installation of two (2) shade structures around the Water Splash Park (Project 1), three bench areas around the play ground (Project 2) and some landscaping improvements (Project 3).



## **Project 1. Splash & Play Shade Structures**

Task 1: Install two shade structures at Splash Park main entrance.

Task 2: Concrete slabs at base of shade structures

## **Project 2. Playground Benches and Shade Structures**

Task 1: Frame and pour concrete bases for benches around playground.

Task 2: Install 3 benches.

## **Project 3. Landscaping**

Task 1: Clear landscape area.

Task 2: Lay weed barrier.

Task 3: Lay and compact crusher fines

**MEMORIAL ROSE GARDEN:** Will involve cleanup of planting zones, planter boxes (1-3), xeriscaping, irrigation and tree planting (Project 4 - Zones A-C); landscaping, irrigation, and tree planting (Project 5); concrete drive pad for RV station (Project 6).



## **Project 4. Redesign and Landscaping of Rose Garden**

- Task 1: Clear vegetation in Zones A-C.
- Task 2: Re-design irrigation system.
- Task 3: Plant rose bushes (Locations 1-3).
- Task 4: Plant three (3) new trees.
- Task 5: Lay weed barrier in Zones A-C.
- Task 6: Lay crusher fines in Zones A-C.
- City Task: Install lighting system at corners of garden (Zones B & C);  
Work to be done by city electric department.

## **Project 5. Landscaping**


- Task 1: Clear and level.
- Task 2: Extend irrigation system for tree locations.
- Task 3: Plant trees.
- Task 4: Lay weed barrier.
- Task 5: Xeriscape (gravel and/or cobble).

## **Project 6. RV Dump Station Drive Pad**

- Task 1: Excavate and frame drive pad.
- Task 2: Pour and surface concrete pad.

**ALTERNATE PROJECTS**

**RIO ANIMAS PARK:** Will include installation of three picnic tables (Alternate 1), construction of input/output ramp for rafting and tubing (Alternate 2), improving the remote parking area (Alternate 3), and construction of a pavilion/ramada for large group gatherings (Alternate 4).

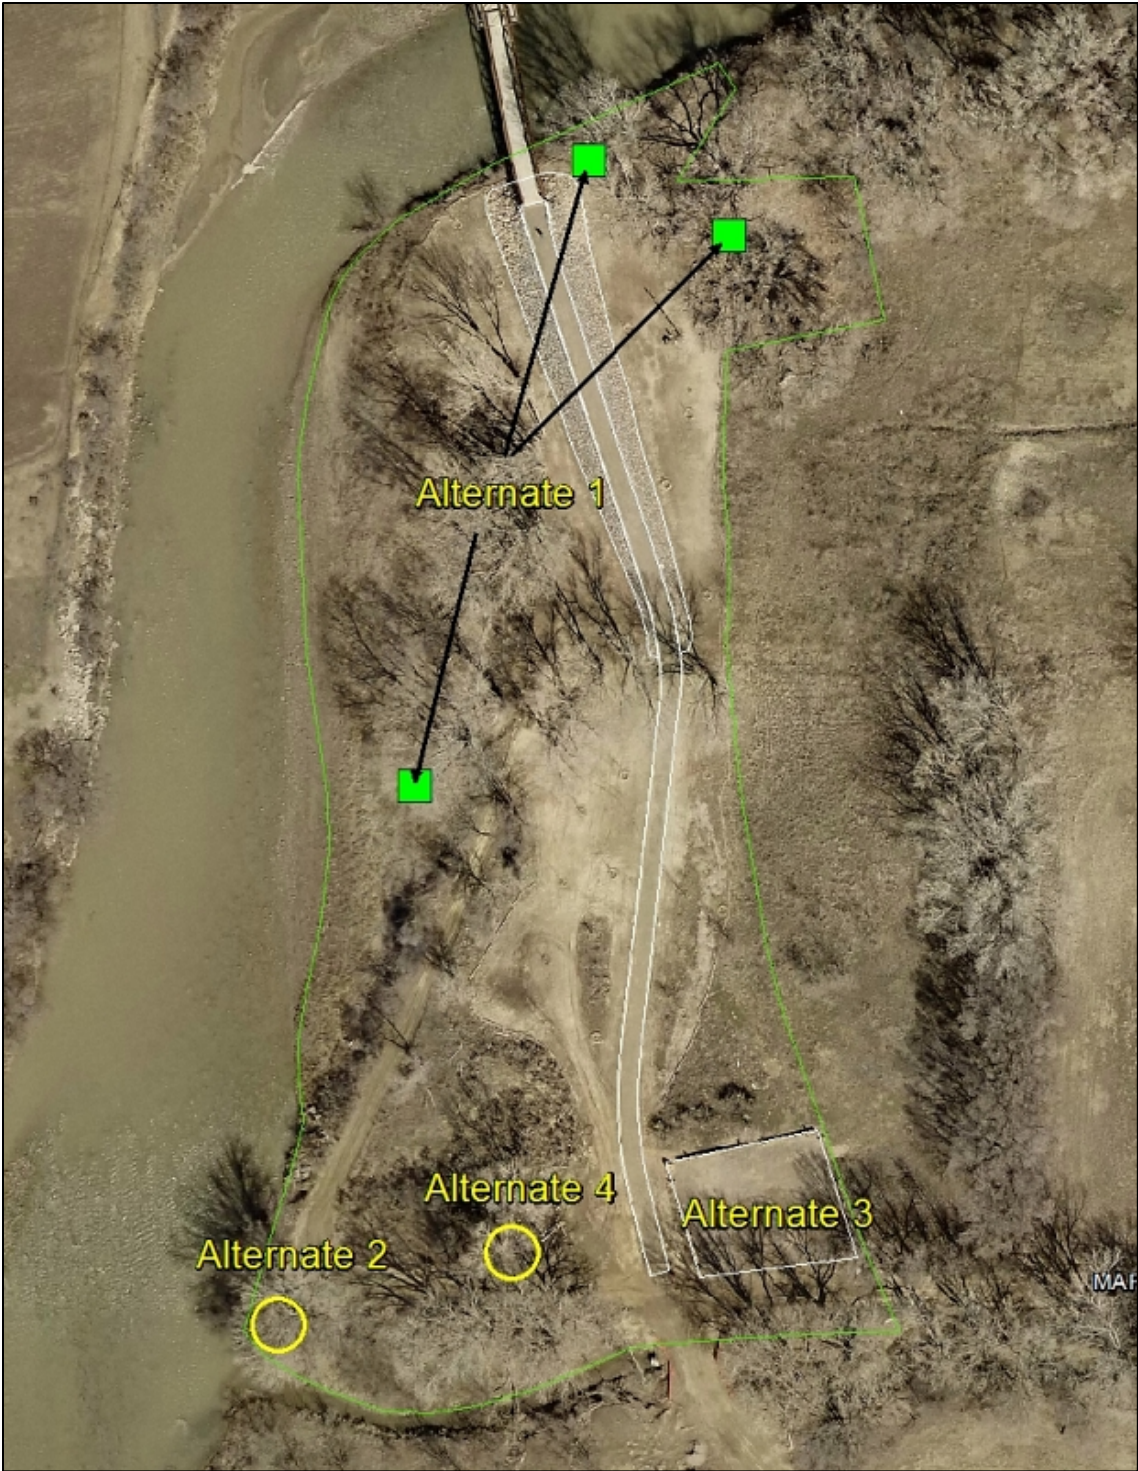

## **Alternate 1. Picnic Tables**

- Task 1: Clear vegetation.
- Task 2: Assemble picnic tables.
- Task 3: Install picnic tables into concrete footers.
- Task 4: Install trash can at each location.
- Task 5: Mulch trail paths to picnic tables.

## **Alternate 2. Input Ramp**

- Task 1: Clear vegetation.
- Task 2: Lay gravel along ramp.
- Task 3: Lay cobble along border of ramp.

## **Alternate 3. Parking Lot Graveling**

- Task 1: Clear vegetation.
- Task 2: Lay and spread gravel.
- Task 3: Install two (2) trash cans.

## **Alternate 4. Pavilion / Ramada**

- Task 1: Clear vegetation.
- Task 2: Construct pavilion/ramada.
- Task 3: Install picnic table, trash can, and grill.
- Task 4: Gravel area.
